

Silver Lake Infrastructure Improvement Project Silver Lake, Minnesota

Project Update



SILAK 171969

Project Contacts

SEH (Engineer)

1390 Hwy 15 S, Suite 200
PO Box 308
Hutchinson, MN 55350

Dillon Boggess

Resident Project Representative
320.333.7545 (Cell)
dboggess@sehinc.com

Sam Fink, PE (Lic. MN, NE)
Project Manager
763.447.1341 (Cell)
sfink@sehinc.com

Brody Bratsch, PE (Lic. MN)
Project Engineer
320.223.8418 (Cell)
bbratsch@sehinc.com

Contractor

R & R Excavating, Inc.
1149 Hwy 22 S
Hutchinson, MN 55350
Office: 320.587.5918

City of Silver Lake

308 Main Street W
Silver Lake, MN 55381
320.327.2412

Diane Petersen
City Clerk


Chris Penaz
Public Works Director

September 16, 2025 | Project Update No. 27

Current and upcoming work includes the following:

- **Lane Avenue from TH7 to Main Street (Area 1)**
 - Seeding and topsoiling late this week or early next week.
- **Center Street from Lane Avenue to Oliver Avenue (Area 2)**
 - Blacktop placement anticipated by week of October 6th.
- **Oliver Avenue from Main Street to Center Street (Area 2), Center Street from Oliver Avenue to Park Avenue (Area 2), and Main Street at Park Avenue (Area 2)**
 - Curb and Gutter placement this week or early next week.
 - Blacktop placement anticipated by week of October 6th.
- **Frank Street from Lane Avenue to Oliver Avenue (Area 3)**
 - Placement of sand, edge drains, and Class 5 this week.
 - Concrete curb and gutter late early next week.
 - Blacktop placement anticipated by week of October 6th.
- **Lake Avenue N and Frank Street (Area 6)**
 - Seeding and topsoiling in place. Please help water your new lawn.
- **Lake Avenue S and Merrill Street (Area 8)**
 - Seeding and topsoiling late this week or early next week.
- **Frank Street-Center Street-East Avenue Loop (Area 11A)**
 - Seeding and topsoiling late this week or early next week.
- **Cleveland Street East (Area 11B)**
 - Concrete curb and gutter this week
 - Blacktop placement anticipated by week of October 6th.

See Project Update No. 26 for *Caring for Your Newly Seeded Area* flier and tips for caring for your new lawn.

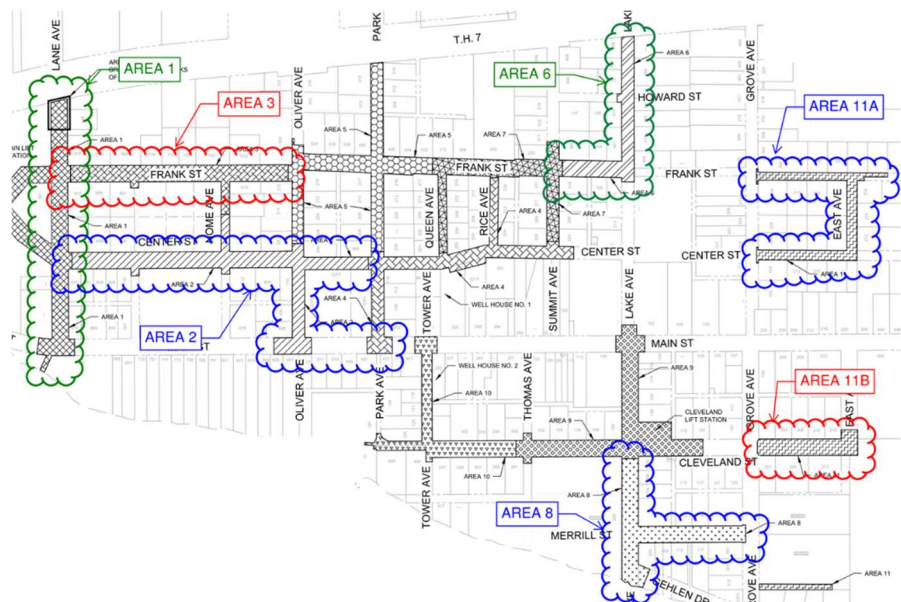

(Continued on Back)

City Email List:

<https://lp.constantcontactpages.com/sl/VQhZlrO>



City Text List:

<https://lp.constantcontactpages.com/sl/OB72rLD>



Concrete that has just been poured needs time to cure. Even though it may look passable, even walking on it may damage the surface. Once the concrete has been poured, a curing compound is placed on the surface to help cure it evenly. This white compound may look like the concrete is dry, but again it is still wet. It takes 7 to 10 days for the concrete to be able to walk on and not do any harm. **Please refrain from walking or riding bikes on the new concrete because those activities may damage it.**

We encourage all residents to sign up to receive the weekly Project Update letters by email. If you are interested in receiving future Project Updates by e-mail, please send your name, property address, and e-mail address to Julie Brinkman at jbrinkman@sehinc.com. (Any mailings will be sent blind copy so that your email address will be kept confidential.) You may also sign up for the City's email or text messaging service to stay up to date on City announcements and updates. Additionally, the City is striving to keep their Facebook page and website updated with pertinent project information.

Thank you for your continued patience and cooperation. If you have any questions or concerns, please contact Dillon, Sam, or Brody.

Short Elliott Hendrickson Inc.
1390 Highway 15 South, Suite 200
P.O. Box 308
Hutchinson, MN 55350-0308



Project Update

Silver Lake Infrastructure Improvement Project
Silver Lake, Minnesota

Affirmative Action–Equal Opportunity Employer
